
TraceBack — Timeline and Gantt Chart

Nov 6, 2026 · @Soumyaranjan

TraceBack went from proposal to a tested, deployed system in 11 weeks (19 Aug to 6 Nov 2026): planning and requirements through September, the whole system built and merged in a four-day implementation sprint (12–15 Oct), deployment to AWS on 3 Nov, and testing, hardening and the final reports on 5–6 Nov. Every date below comes from Jira, the git history, file and server timestamps, or the test logs.

Gantt chart

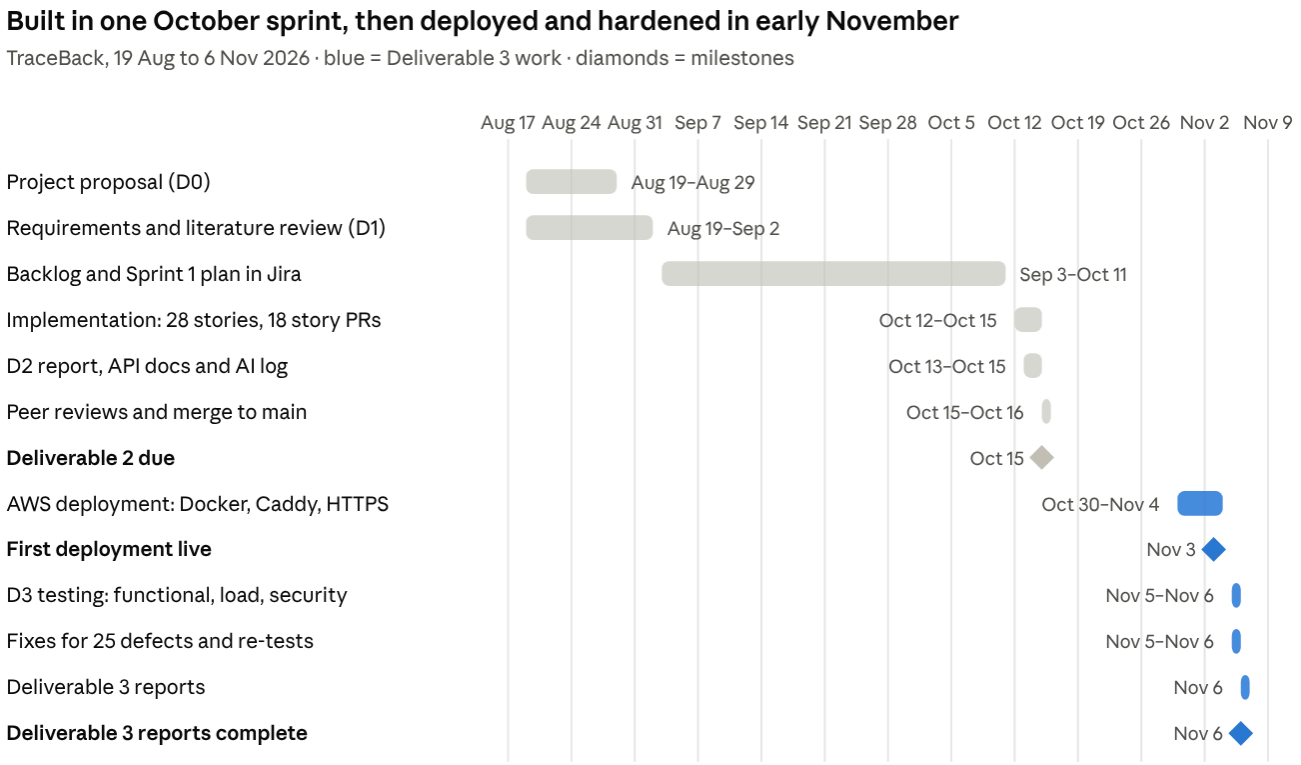

Jira sprints (Deliverable 2 report, section 8), git history of cs455project/campus-lost-and-found and branch d3/integration, server and test logs

Phases and milestones

Phase	Dates	Owner	Output	Evidence
Sprint 0: proposal	19–29 Aug	Whole team	Deliverable 0, the project proposal, submitted 29 Aug	`Deliverable_0/` in the repository (commit of 29 Aug)

Phase	Dates	Owner	Output	Evidence
Sprint 0: requirements	19 Aug – 2 Sep	Whole team	Deliverable 1: requirements, user stories, literature review; Sprint 0 closed with 4 of 4 items done	Jira sprint report (D2 report, figure 26)
Backlog and Sprint 1 plan	3 Sep – 11 Oct	Whole team, led by Rohit Yadav	28 user stories with epics, estimates and assignees; Sprint 1 planned with 10 foundation items (40 story points)	Jira backlog (D2 report, figure 25)
Implementation sprint	12–15 Oct	All six members, one module each	Schema and sign-in (12 Oct), reports, custody and claims (13 Oct), the AI layer (14 Oct), 18 story pull requests (15 Oct)	13 database migrations dated 12–14 Oct; PRs #11–#28
Reviews and merge	15–16 Oct	Every member reviewed 6 PRs; Rohit Yadav merged	All 18 PRs merged into `main`, 0 conflicts, 189 tests passing	Merge commits on `main`, 15 Oct 22:12 to 16 Oct 02:24
Deliverable 2	due 15 Oct	Whole team	Report, API documentation, OpenAPI file, AI Engineering Log (26 entries)	`Deliverable_2/`
AWS deployment	30 Oct – 4 Nov	Soumyaranjan Sahu	Docker Compose and Caddy setup, one-command deploy script; site live over HTTPS on 3 Nov; real email checked on 4 Nov	`deploy/` folder; server deploy log

Phase	Dates	Owner	Output	Evidence
Deliverable 3 testing	5–6 Nov	Soumyaranjan Sahu	Unit, integration, system, adversarial, concurrency, load and failure tests; 270 new automated tests	`testing/results/` (JUnit file of 6 Nov)
Fixes and re-tests	5–6 Nov	Soumyaranjan Sahu	25 defects fixed, every suite green on the final code	14 commits on `d3/integration`
Deliverable 3 reports	6 Nov	Soumyaranjan Sahu	The reports in this document	This document

What the schedule shows

- **Planning paid off.** Stories were split by module before coding started, so six people built and merged 18 pull requests in four days with no merge conflicts.
- **AI assistance compressed the build.** About 13,300 lines of product code would take roughly 36 person-months by a classic estimate (Costing tab); the team did it in one sprint with an AI coding assistant, checking and correcting its output (AI Engineering Log).
- **Testing came late and found real problems.** The load, concurrency and failure tests in November found 25 defects, including one critical; all were fixed before the reports. For future work, running these suites from the first sprint would catch such problems earlier.
